Sprint 2 Intermediate Product Report
Team Name: IEEE Impact & Platform Leveraging Data Mining Analytics and AI for Automated Impact Assessment and Quantification

Team Members: Waleed Alfar, Christina Phan, Johnessa Barroquillo, Caden Foley, Michael Hawes
Sponsor: Matthew Scott

Date: 10/12/2026

1. Overview

Provide a brief overview of the Sprint goal and the work completed. This is the goal defined during the Planning phase.

- **Sprint Goal**: The goal for sprint 2 is to research and develop system specifications for the different assigned modules. Each module's owner is responsible for developing system specifications and a product plan for the development of their module, which includes specific technologies to be used and plans for alternatives. We are also asked to merge our modules into groupings, such that plans exist for unified supermodules encompassing multiple people's individual modules.
- **Work Completed**: The team has built plans for the development of each individual module. These include a specification document and a product charter for each module. We have also made documents for combined modules, and planned for the eventual grouping of all the modules into a single unified product.

2. Achievements

- List the user stories (not the tasks) developed during the sprint. Update the status for each of the user stories (including their tasks) in the Taiga (or equivalent) board.

- **User Stories**:
    - Buddy System module specification document
    - Buddy System module Product Charter
    - Relevance & Professional Identity module specification document
    - Relevance & Professional Identity module Product Charter

- Wish to Next Move module specification document
- Wish to Next Move module Product Charter
- Game mechanics, impact score + growth feedback module specification document
- Game mechanics, impact score + growth feedback module Product Charter
- Living Ecosystem & Opportunity Engine module specification document
- Living Ecosystem & Opportunity Engine module Product Charter

3. Risk Management

Risk Identification and Assessment

Identify potential risks in various categories and assess the likelihood and impact of each risk.

Foreseen Risks and Challenges

[Describe accuracy on the foreseen risks and challenges considering: technical risks, external risks, organizational risks, project management risks, team risks, if applicable]
We have observed many risks in our planning stages. We know that unclear requirements can be disastrous to our final product. Additionally, there are dark patterns that our eventual app may contain if we do not plan accordingly. We need to ensure that the Impact++ app is as fair and impartial as possible, while also supporting developing creators. Another risk that we have foreseen is incompatibility between our modules. It's possible that if we don't plan properly, we will be in a situation where we do not have compatible code, which will cause excessive stress.

Report Unexpected Risks and Challenges

[Describe unexpected risks and challenges considering: technical risks, external risks, organizational risks, project management risks, team risks, if applicable]
Some unexpected risks come from time management, as important parts of the project were scheduled during midterms, which caused a large amount of stress. However, we worked through this, and made sure to allocate enough time each week to stay on track. Other unexpected risks came from specific research topics, such as the unexpectedly small niche for mentorship / buddy applications.

Update Ongoing Risk Management

Update the risk management section front the sprint planning at this stage by explaining how risk assessment and management will be addressed in this sprint to ensure emerging risks are managed proactively and continuously.

Our team has been proactive in seeking out potential risks and acting on them. The largest risks are scope-creep and misaligned work. We don't want to be in a situation where each person's work is impossible to combine into a cohesive product. In order to fix this, we make sure to bring up our plans for our modules in each standup meeting, which we are still doing twice per week. Additionally, we are already working on cohesive plans for combining certain modules, so we know exactly what we will need to put together.

Incorporate Risk Management

Describe risk management into your Sprint Backlog to ensure proactive risk management and maintain project stability.


We have been communicating with each other to ensure that each of our plans for the product specifications are compatible. We make sure to discuss different technologies before settling on them, and we make sure that everything will work together seamlessly. We are also communicating with our product owners frequently and receiving constant feedback from them. We are navigating scope-creep by discussing which features we plan on adding, and which we are to avoid.

4. Contribution Metrics

Include the following metrics:.

- **Overall Team Velocity**: 17 tasks completed
- **Velocity by Each Team Member**:
    - Caden Foley: 4 tasks completed
    - Waleed Alfar: 3 tasks completed
    - Christina Phan: 3 tasks completed
    - Michael Hawes: 3 tasks completed
    - Johnnessa Barroquillo: 4 tasks completed
- **Chart of Historical Velocity**:
    - Team Average: 3.4

- Individual Team Members:

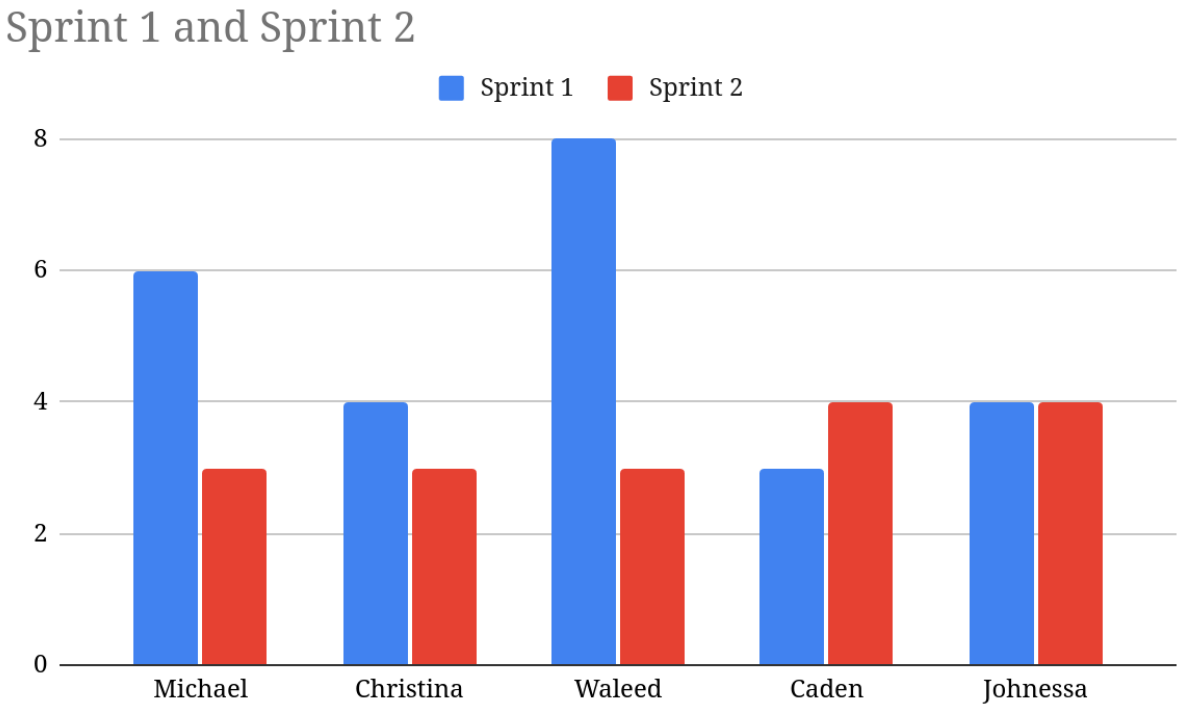


- **Accuracy of Estimated Effort**: 95%, the estimated effort varies to some degree, but it is largely accurate.

5. Evidence

- Taiga Board: https://tree.taiga.io/project/michael_hawes-ieee-impact-product-backlog/timeline
- GitHub Repository: N/A (Under an NDA and no coding has started yet)
- https://docs.google.com/document/d/1dhOklukwb9yKGVR1WW9HYrO0scjhv5KW/edit?usp=sharing&ouid=109592528273182120467&rtpof=true&sd=true
- https://docs.google.com/document/d/1eebEmXZZz-cxsUNx7jgCIIdtCQnZjJwz/edit#heading=h.s07wpou0x5ky
- Repo for just the README requirement: https://github.com/waleedalfar/IEEE

- Contributor's Graph:

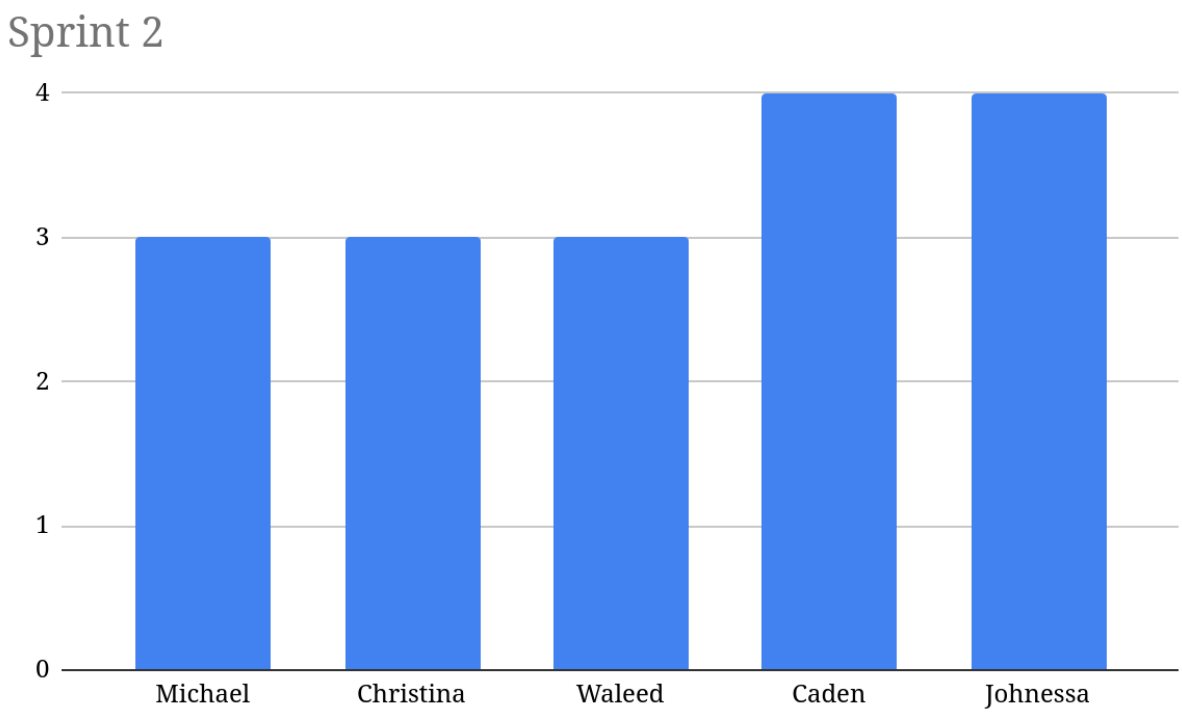

- Explanation of Outliers:
    - If one or more team members have a low velocity, please explain the circumstances and how this will be remedied in the future:

We all completed roughly the same amount of work. This sprint had tasks that were more significant than last sprints, so while we completed fewer tasks overall, the work was constant between sprints.

6. Feedback Summary

Summarize any feedback received from Customer/Product Owner and how it was addressed.

- **Feedback Summary**: Our product owner wanted the team to be split into two subteams for this sprint, one with Christina and Michael, and one with Caden, Johnessa, and Waleed.
- **Addressed Feedback**: We made sure to structure our teams in this way.

7. Updates

Adjustments, new or withdrawn EPICs/user stories, and changes in priority.

- **Adjustments**:

    - We have shifted from developing frontend prototypes to planning the technical specifications of the product.
- **New or Withdrawn EPICs/User Stories**:
    - The only change in EPICS was the addition of the specification step which we are currently working on. We will begin working on code next.
- **Changes in Priority**:
    - The development of code is now a lower priority than the planning and specification stage.

8. Signature from the Product Owner/Client

- 
